

Capital Projects



Capital Projects Update – South Jordan Downtown 11000 South TRAX Station and Midvalley Express (MVX)




South Jordan Downtown 11000 South TRAX Station



South Jordan Downtown 11000 South TRAX Station: Project Information


- New Trax Station on existing red line rail
- Provides transit access to new development in South Jordan including the new baseball stadium

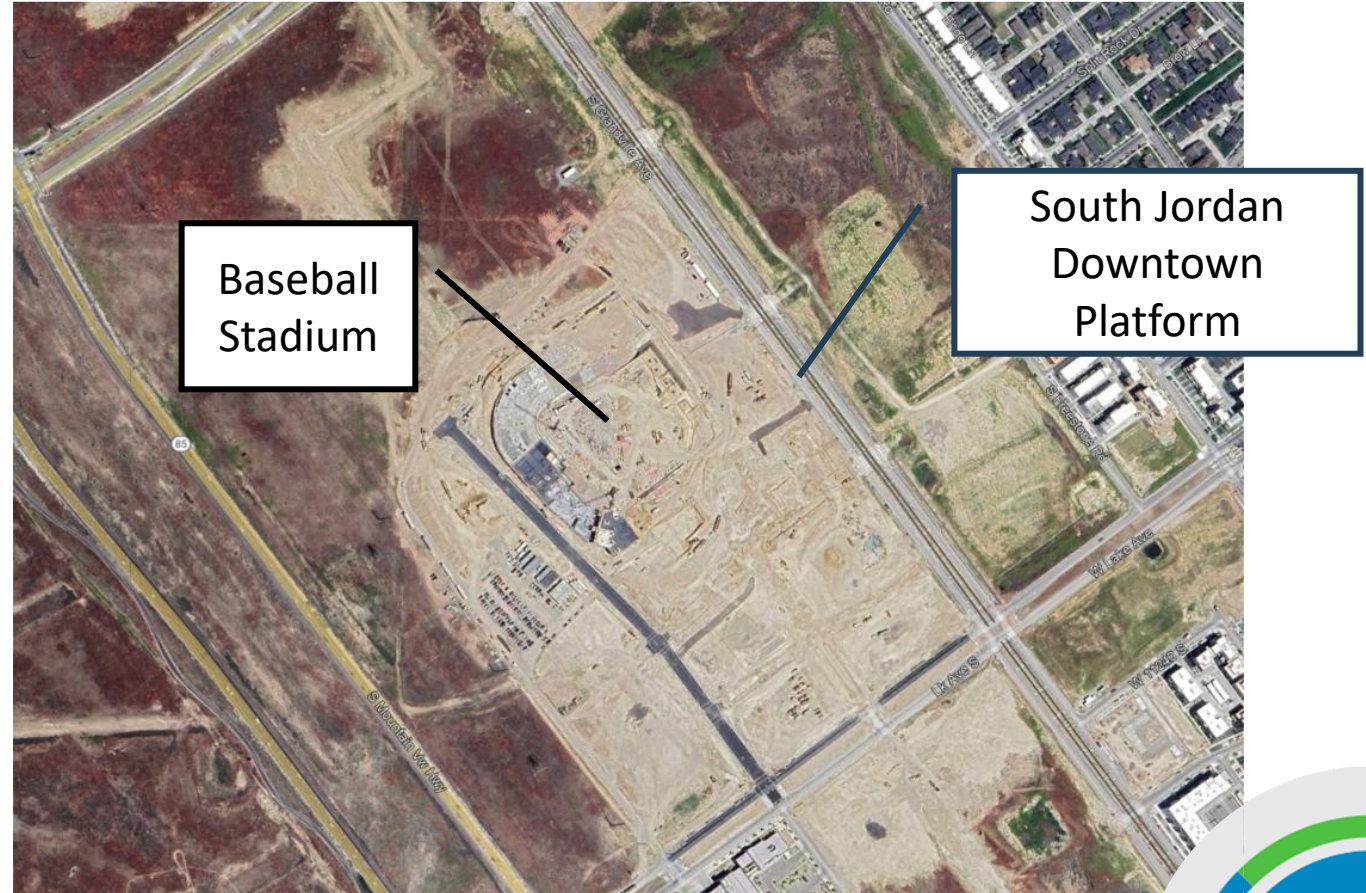

South Jordan Downtown 11000 South TRAX Station: Construction Update

- Construction
 - Final electrical and data installations
 - Testing and commissioning snow melt system
 - Sign installation
 - Network equipment installation and testing
 - Fare equipment installation and testing
- UTA
 - Operator testing
 - Activation process
 - Start of revenue service

First home game April 8th, 2025

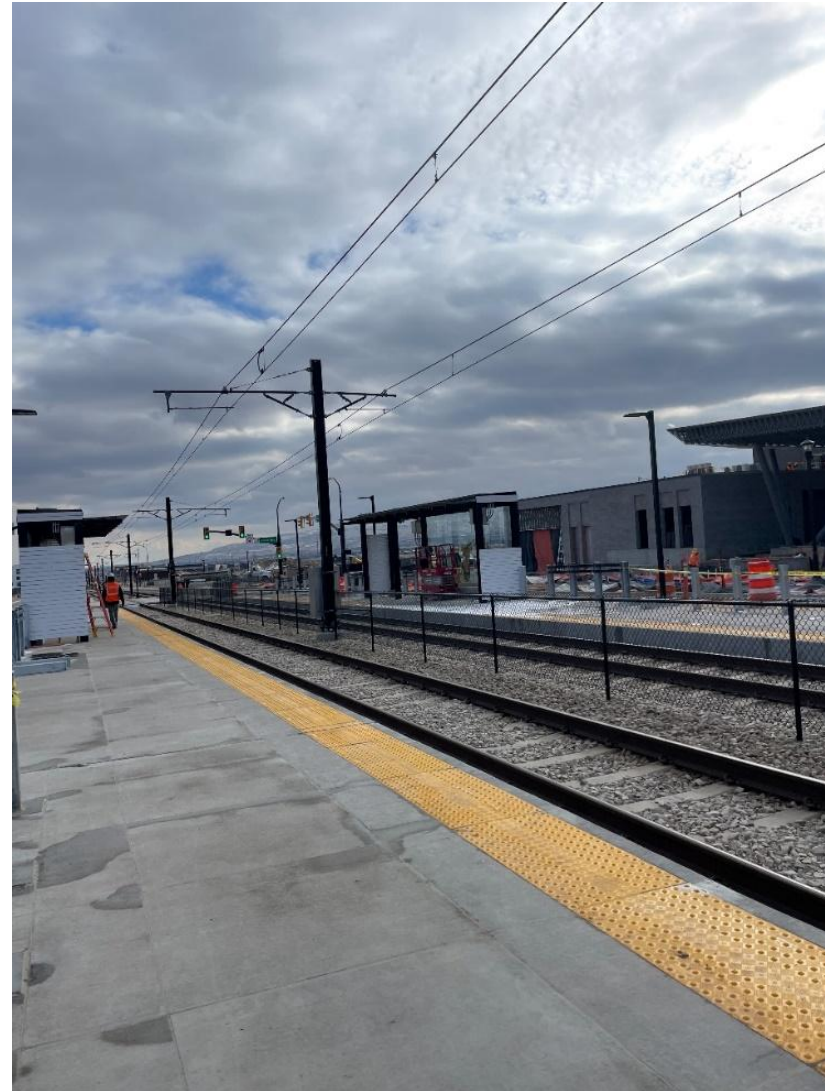


Agenda Item 6. a.



South Jordan Downtown 11000 South TRAX Station: Funding


- Funding Sources
 - TTIF = \$4,200,000
 - SB-006 2024 = 1,050,000
 - Salt Lake County = \$750,000
 - Total Project Budget = \$6,000,000
- Update January 2025
 - % Total Budget Expended = 69%
 - % Construction Contract Awarded = 100%
 - % Physical Construction Complete = 83%

South Jordan Downtown Trax Station Financial Outlook
Budget \$6,000,000

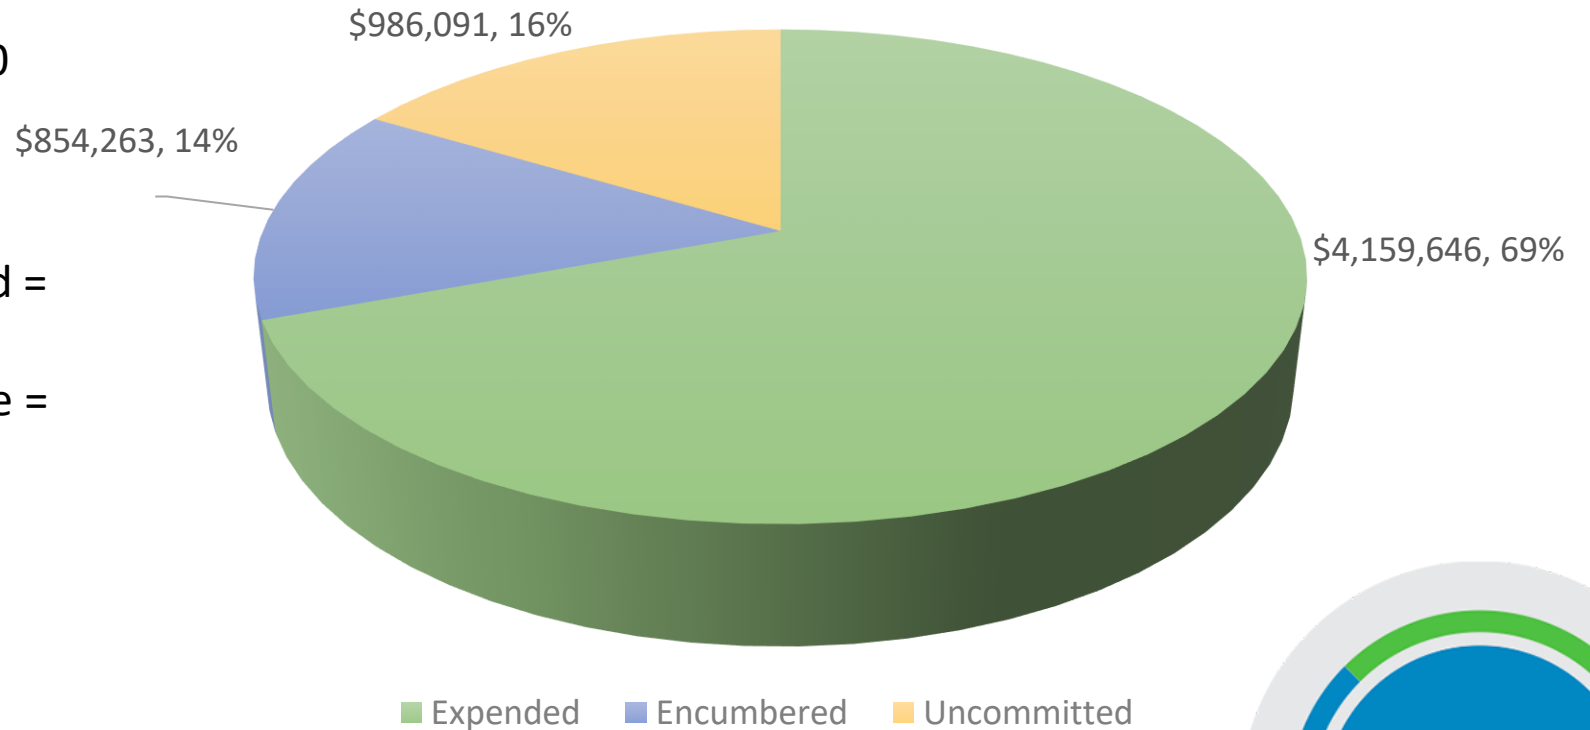

South Jordan Downtown 11000 South TRAX Station

UTAH TRANSIT AUTHORITY

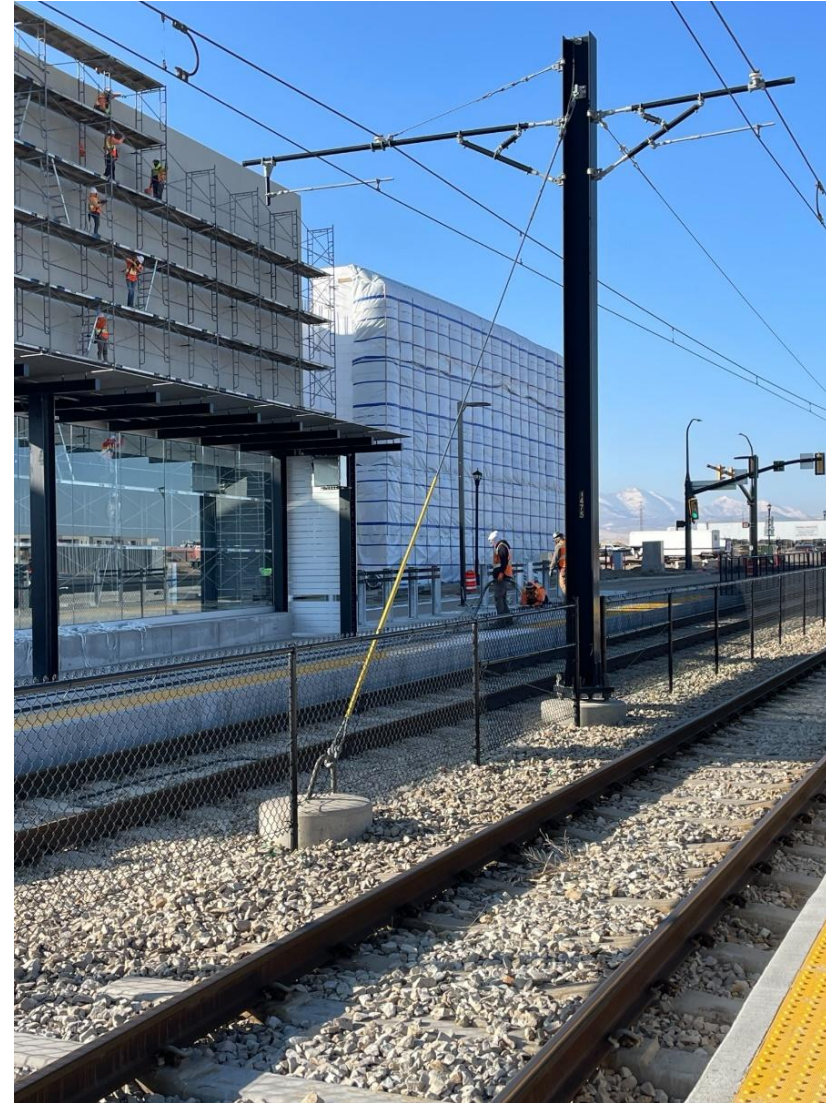


Agenda Item 6. a.



South Jordan Downtown 11000 South TRAX Station

UTAH TRANSIT AUTHORITY

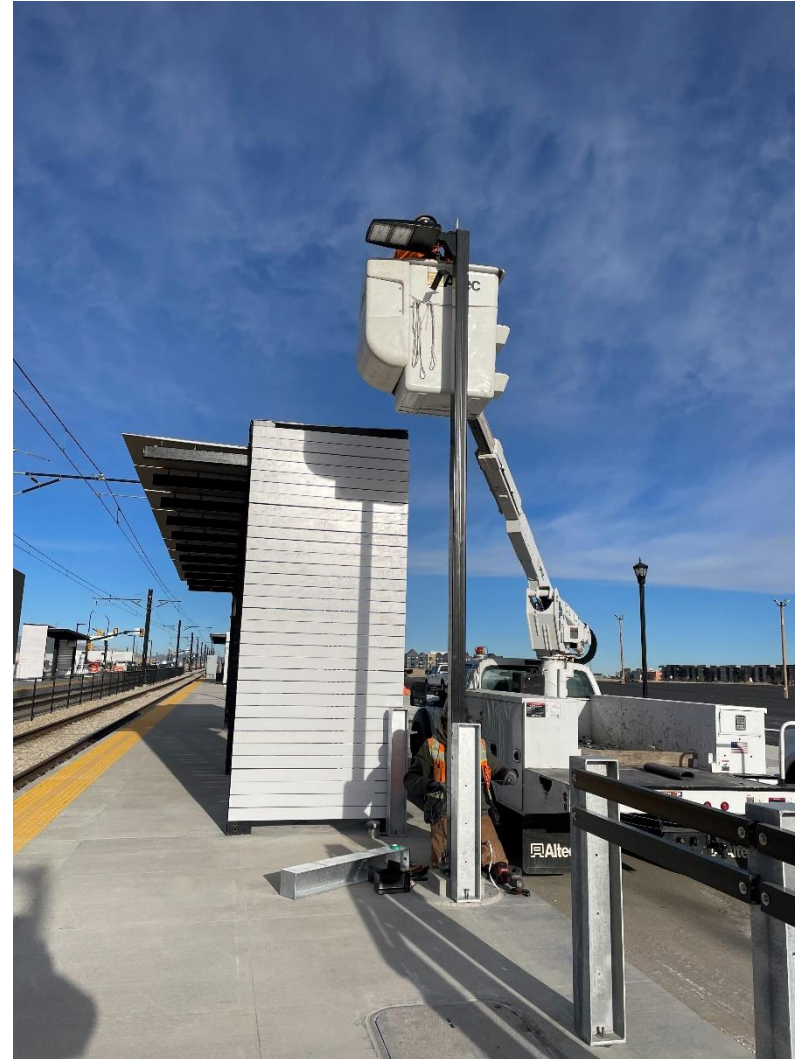

Agenda Item 6. a.





Midvalley Express (MVX)



Midvalley Express (MVX): Project Information

- BRT Route
- 7-mile corridor
- 1.4 miles of exclusive bus lanes
- 15 station locations and 25 platforms
- 10 electric buses will run on the corridor (not funded with this project)
- 1900 riders per day from existing route 47 & 227
- 15-minute peak service

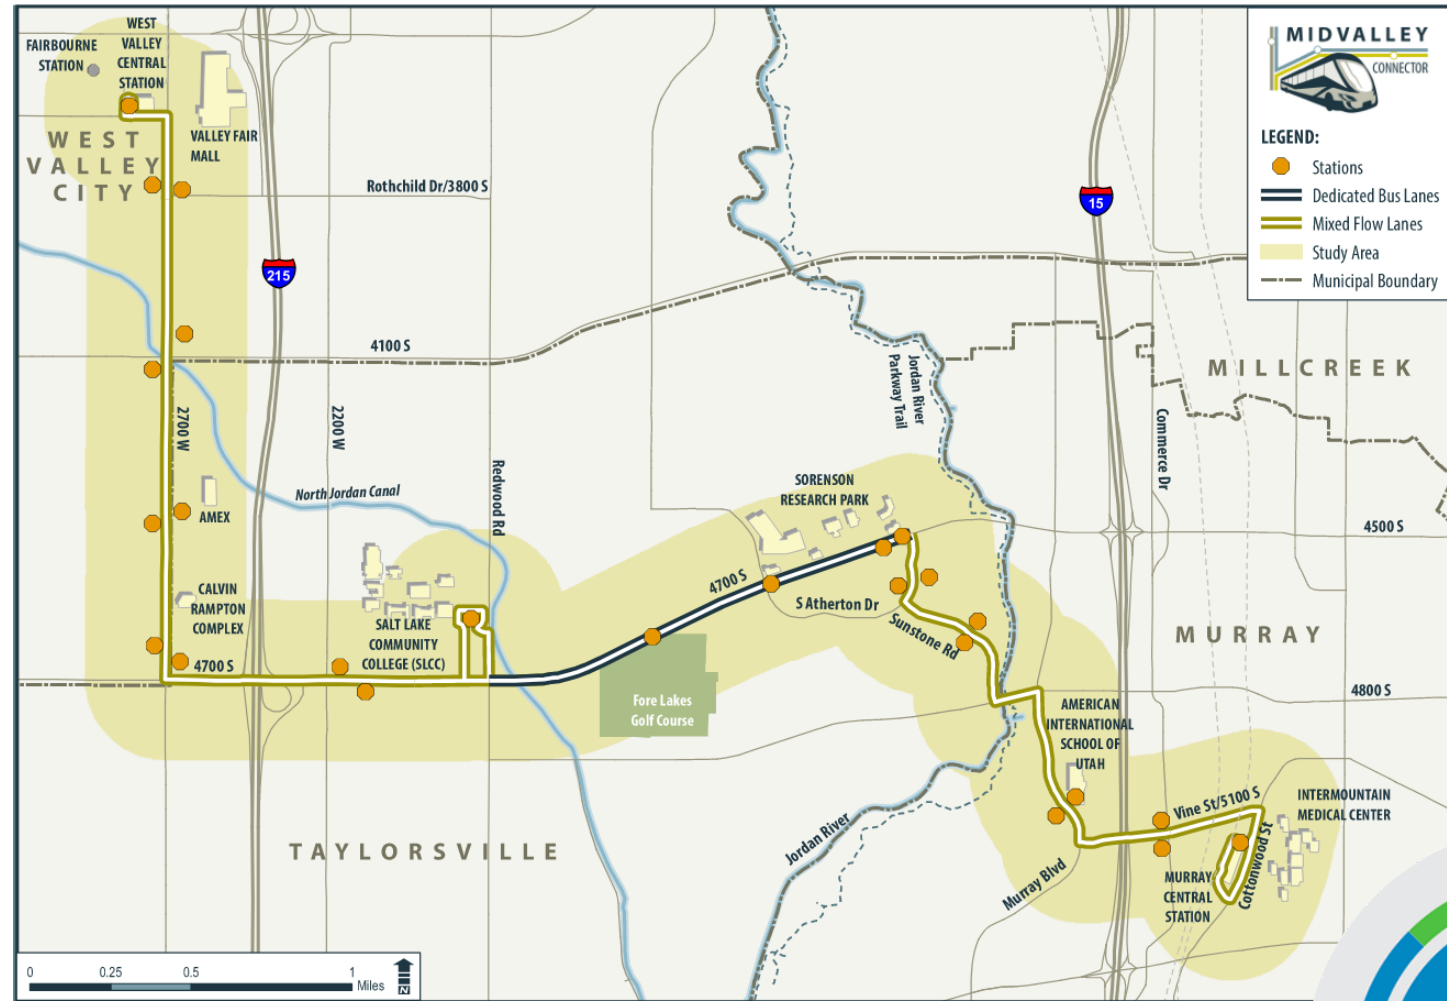


Midvalley Express (MVX): Construction Update

- Construction
 - Utility work along 4700 South ongoing
 - Boring work ongoing
 - Station work ongoing
 - SLCC work nearly completed
 - Wall installation on 4700 South finished except painting
- Lease/Utility Agreements
 - All lease agreements signed
 - All utility agreements signed



Midvalley Express (MVX): Right-of-Way

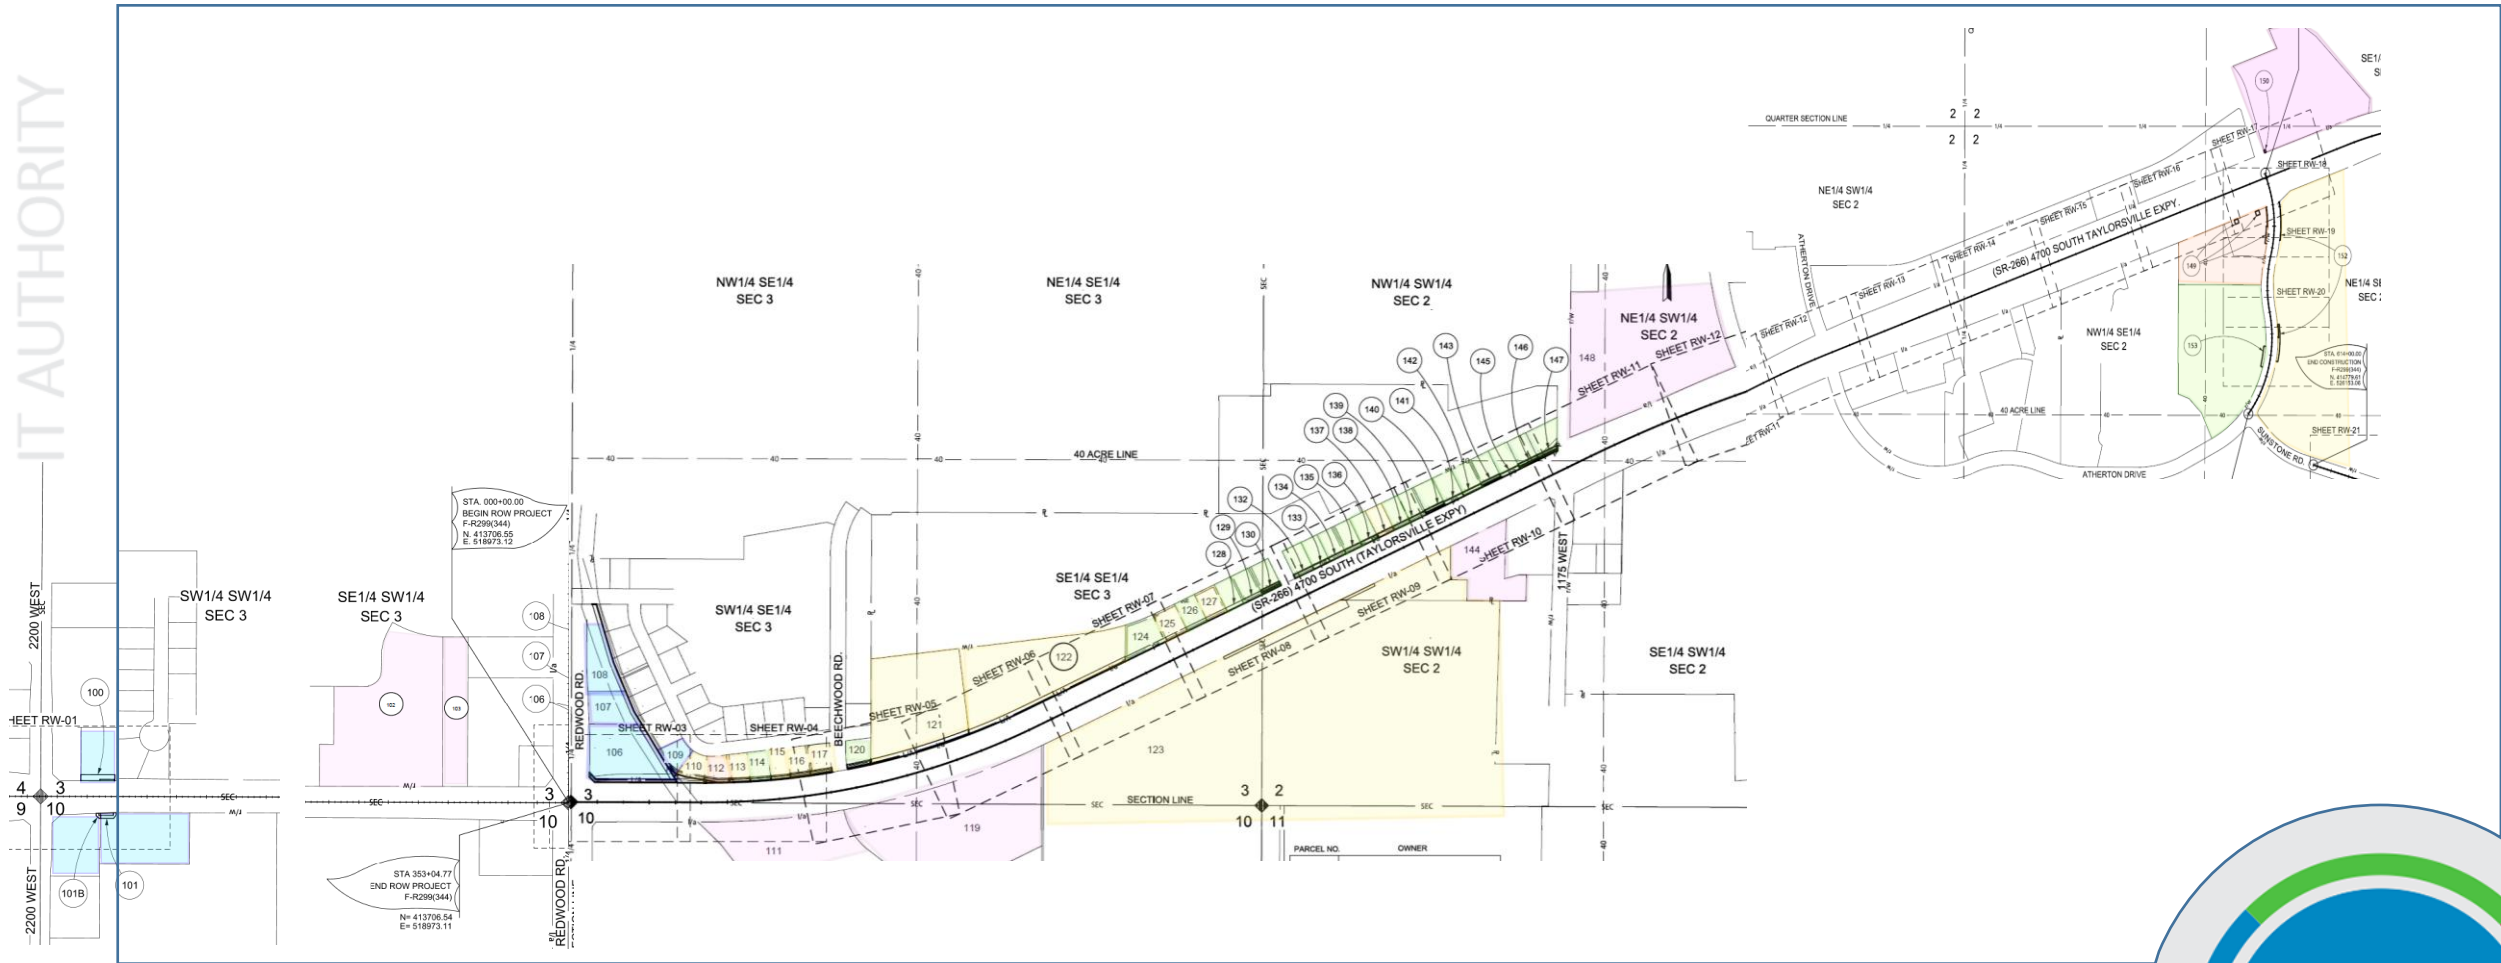

• 57 parcels

• 51 finalized

• 6 to be finalized


Agenda Item 6. a.



Midvalley Express (MVX): Funding

MVX Financial Outlook
Budget \$104,111,800

- Small Starts Grant Agreement Awarded December 2024
- Update January 2025
 - % Total Budget Expended = 25%
 - % Construction Contract Awarded = 100%
 - % Physical Construction Complete = 32%

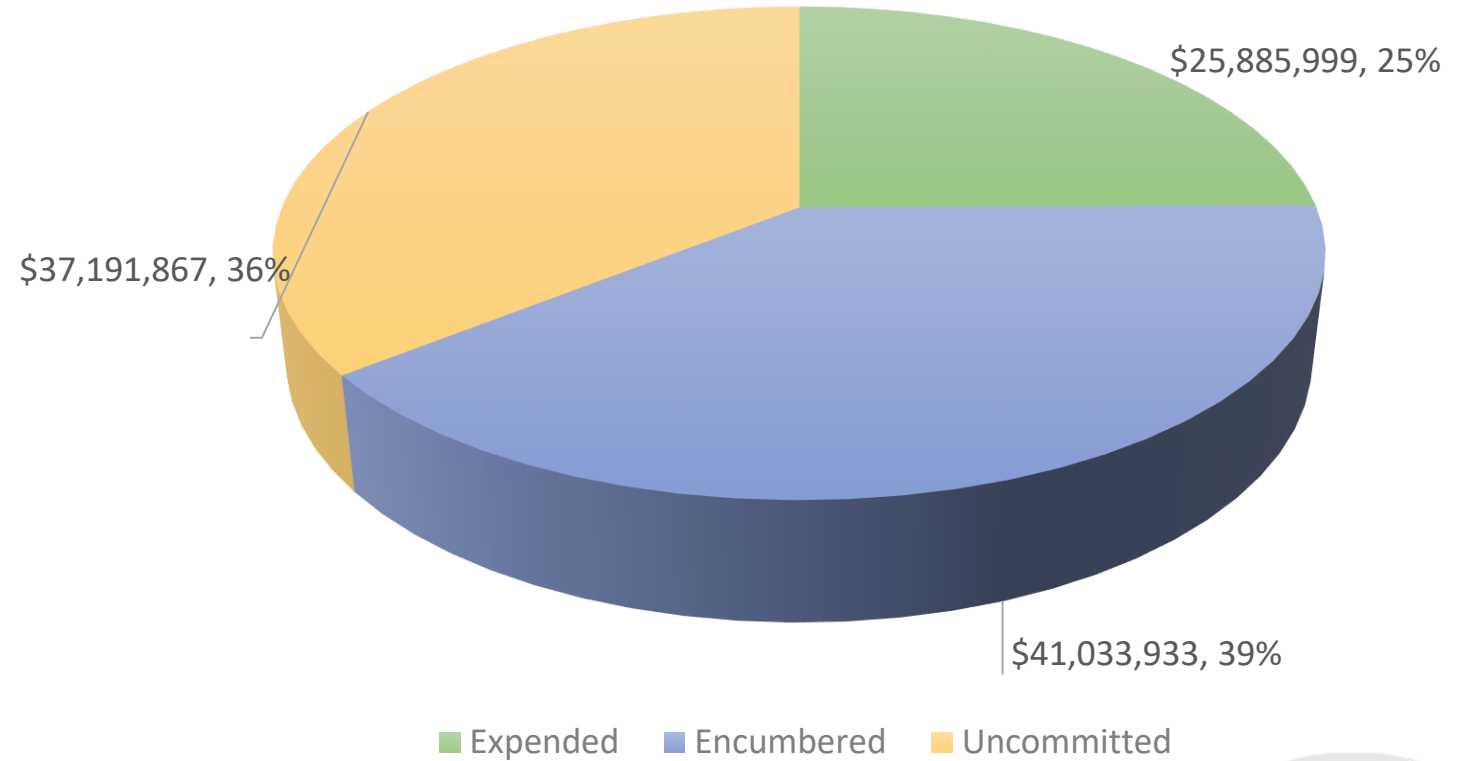

Midvalley Express (MVX): Groundbreaking



Midvalley Express (MVX): FTA Small Starts Grant Approval



UTAH TRANSIT AUTHORITY



Midvalley Express (MVX): SLCC Bus Depot

UTAH TRANSIT AUTHORITY



Agenda Item 6. a.



Midvalley Express (MVX): Canopy Installation



Questions?

